2018 - 2019 CONSTRUCTION PROGRAM

		Status
Road Maintenance	Construction Crew	Ongoing
Lake Magenta Road	Form and Sheet 5km	Completed
Jacup North Road	Form 3km, sheet and seal	Completed
Brook Road	Form and sheet 3km	Completed
Jerramungup North Road	Form and sheet 3km	Completed
Stock Road	Remove Vegetation and Widen Formation	Completed
Cowalellup Road	Form and sheet 3km	Gravel to be Sourced
Rabbit Proof Fence Road	Form and sheet 3km	Completed
Meechi Road	Install Culverts Stabilise Backfill and Realign Curve	Ongoing
Dillon Bay Road	Gravel Sheet 2.3km	Project Postponed
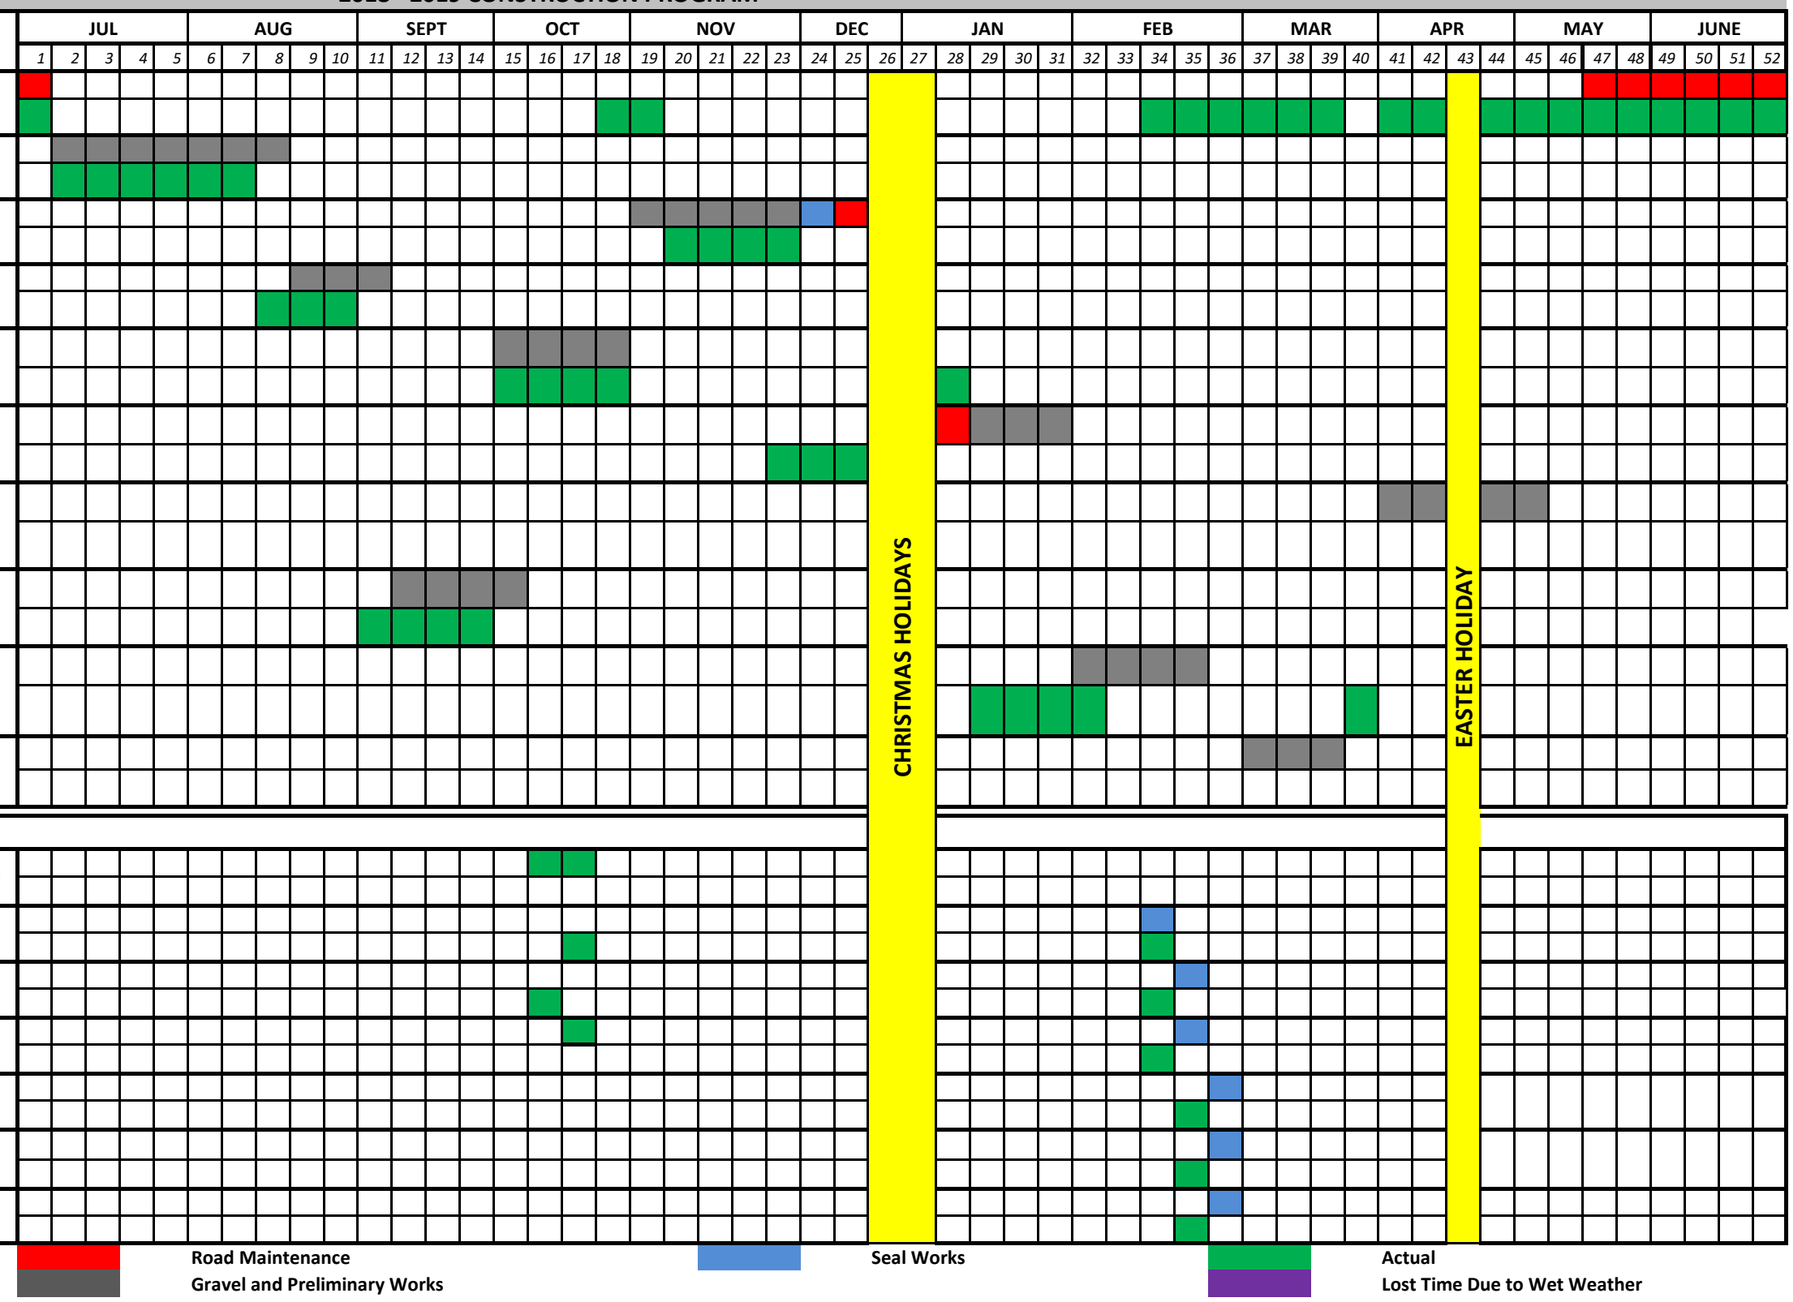
SUBCONTRACTORS		
Gairdner South Road	Pavement Repairs & Second coat seal 5km	Pavement Repairs Completed
Devils Creek Road	Pavement Repairs & Second coat seal 5km	Sealing Completed
Needilup North Road	Pavement Repairs & Second coat seal 5km	Sealing Completed
Borden Boxwood Road	Shoulder repairs and seal widening	Sealing Completed
Black Rocks Road	Second coat seal 3km	Sealing Completed
Jerramungup Townsite	Re-seal Jerramungup Steets	Sealing Completed
Bremer Bay Sreets	Seal Bremer Bay Steets	Sealing Completed
